



2025 Neighborhood Infrastructure Improvements Construction Update #4 – 6/20/2025

What has happened during the past week?


- Sanitary improvements were completed along 1st Street.
- Watermain improvements continued on 1st Street.
- Sanitary sewer and water service installations to individual homes were completed on Fraiser Street.
- Storm sewer improvements were completed on 1st Street West of Farm Street.

What is scheduled for the week of June 23rd?

- Street removals will begin on Farm Street.
- Concrete curb and driveway pour backs will begin and be completed on 1st Street West of Farm Street, 1st Place, Fraiser Street, and Olive Street.
- Watermain improvements will continue on 1st Street.
- Sanitary sewer improvements on Farm Street will begin. We will begin with hooking residents up to temporary water. Impacted residents have received a additional notice via door hanger.
- Storm sewer improvements on 1st Street will continue.
- Final testing on water main was completed on Fraiser Street. We will begin switching residents from the temporary water system to the newly installed water main. Impacted residents have received additional info via door hanger.

Important Notes

- PLEASE DO NOT TOUCH the installed wooden stakes, as they are critical for construction.
- Please refrain from parking on streets under construction from 7 AM to 7 PM

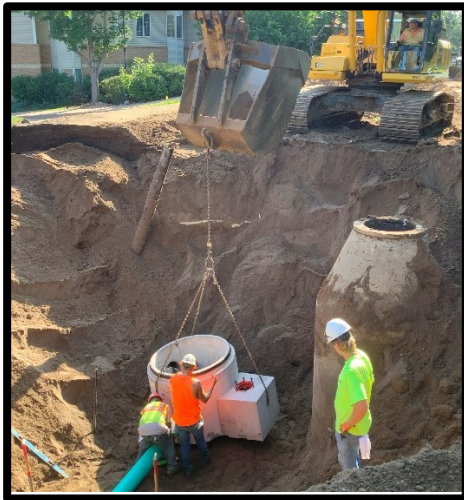

Sanitary sewer improvements



Water Service Replacements

Questions or Concerns? Please Call the Hastings Engineering Department at **(651) 480-2334**

Spread the Word & Subscribe to E-Updates!

- Text Alerts Sign up for SMS text updates by texting **25STREETS** to **651-349-9255**
- Email Updates..... Sign up at www.hastingsmn.gov/enotify
- Website..... www.hastingsmn.gov/2025Streets
- Printed Notices.....Watch for mailbox updates and door tags
