



2025 Neighborhood Infrastructure Improvements Construction Update #18 – 9/26/2025

What has happened during the past week?

- Boulevard restoration continued throughout the project.
- Final grading and blown compost seeding were completed.
- Final paving was completed.

What is scheduled for the remainder of 2025?

- Road striping will be completed on 1st Street next week.
- Watering of the new seed will continue.
- New street signs will be installed.
- Construction signs will be picked up.
- Final street and boulevard cleanup will be completed.
- Erosion control devices will begin to be removed where we have 70% or more of turf re-established, or after the first week of freezing weather.


What is scheduled for 2026?

- We will complete a restoration walkthrough in the spring to ensure all seed is growing, and we will have the contractor touch up areas not fully established as needed.
- We will also complete a concrete warranty walkthrough in the summer of 2026 to replace any damaged or cracked concrete.

This will be the final update for the 2025 Neighborhood Project. We thank you all for your patience and cooperation during this project!



Final paving

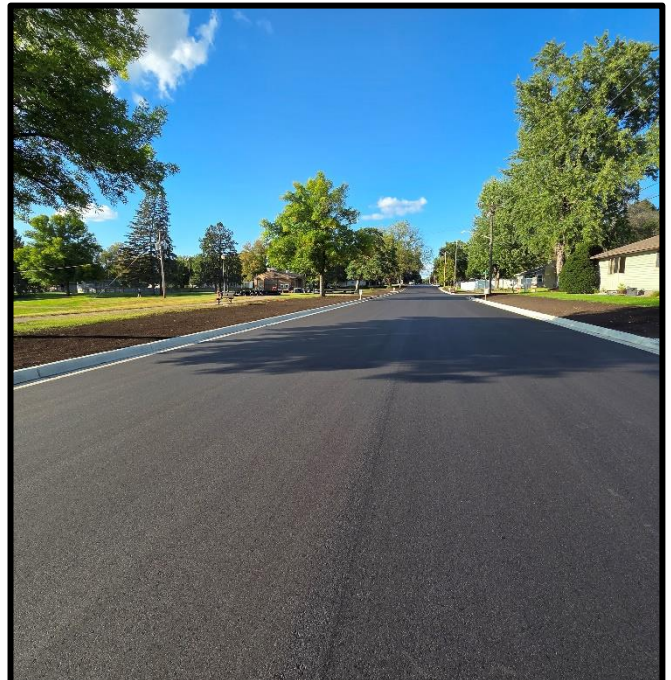

State Street after final paving
