



2020 Neighborhood Infrastructure Improvements Construction Update #20 – 10/22/2020

What has happened during the past week?

- Final site cleanup and minor final construction activities have been ongoing.
- Preparations in advance of final paving have been completed.

Weather dependent, final paving is scheduled on 15th St E, Cannon St, 22nd St, 23rd St, 24th St & 25th St on Friday, October 23rd and will be completed by the end of the day. Affected residents will be receiving door to door notices on this work. Please do not park vehicles on these streets Friday so work can proceed unimpeded.

What is scheduled for the week of October 26th?

Final Site Cleanup: As final paving and restoration is completed the contractor will be doing general site cleanup and taking care of miscellaneous construction items needed to complete the project. Hauling away debris, removing traffic control, hauling out equipment & materials, etc. will be ongoing throughout the week.

*****IF YOUR MAILBOX WAS REMOVED DURING CONSTRUCTION AND HAS NOT YET BEEN REINSTALLED*****

Please notify the Engineering Department and place your mailbox in your front yard so the contractor can reinstall it. Temporary mailboxes will be removed and mail will be returning to regular delivery once final paving is completed and all mailboxes have been reinstalled.



An example of final paving operations in progress.



A tack truck applying tack coat in advance of the final layer of pavement. Tack coat ensures that the final layer of asphalt will bond to the lower layers to stay in place.


Who do I contact with questions or for assistance? Project management services are being provided by the City's Engineering Department. The department can be reached at **(651) 480-2334** with project questions and concerns.

Spread the Word & Encourage E-Updates! Please make sure to share this information with your neighbors and tenants, and encourage them to sign up for at least one of the two electronic updates options if they have not yet done so!

- **E-Notifications** - Sign up for email updates on our website at www.hastingsmn.gov. Click on the *E-notifications* button at the bottom of the page, and sign up for "2020 Neighborhood Infrastructure Improvements".
- **Text Messages** – this is a great way to have the information in the palm of your hand! You'll receive a weekly text message from us with a direct web link to the current construction update. Text **2020STREETS** to **888777** to enroll. Reply STOP at any point to opt out.



15th St Area

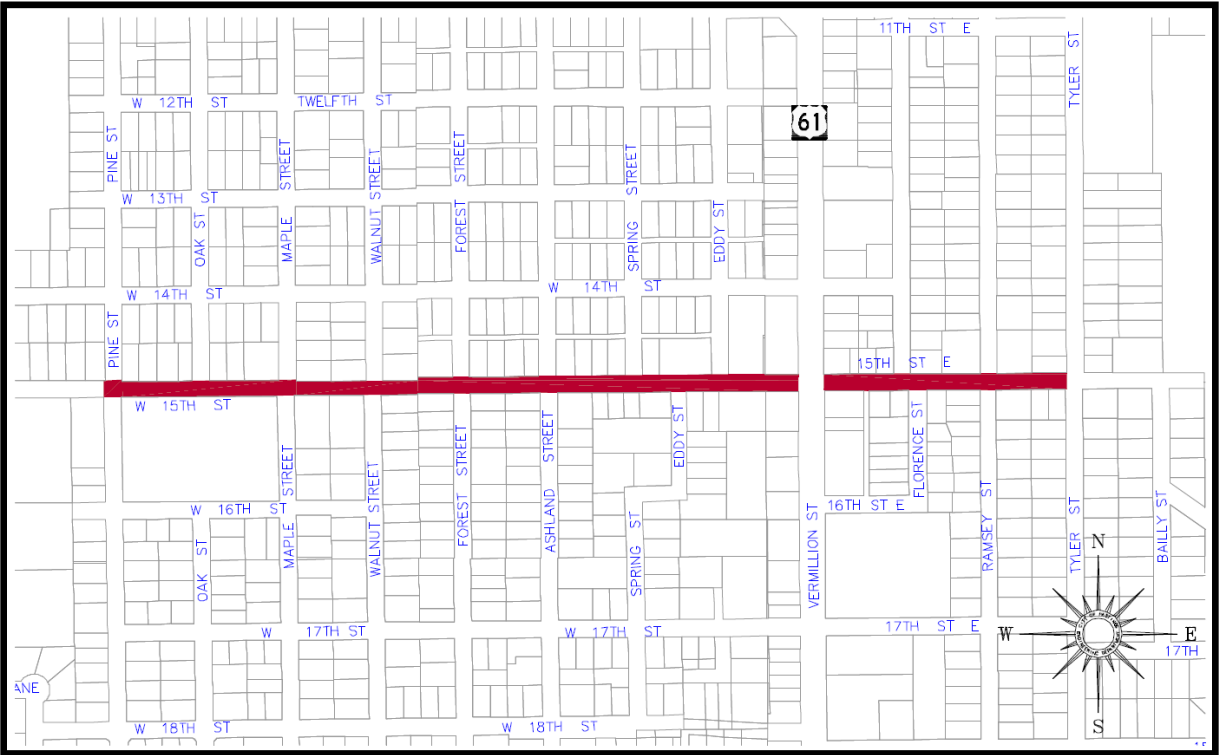

Cannon St Area

