



## 2020 Neighborhood Infrastructure Improvements Final Construction Update– 10/30/2020

### What has happened during the past week?

- Final site cleanup and minor final construction activities have been ongoing.
- Preparations in advance of final paving have been completed.

### What work is scheduled for the week of November 2<sup>nd</sup>?

**Weather dependent, final paving is scheduled to begin on Cannon St, 22<sup>nd</sup> St, 23<sup>rd</sup> St, 24<sup>th</sup> St & 25<sup>th</sup> St on Monday, November 2<sup>nd</sup> and will be completed on 15<sup>th</sup> St E on Tuesday, November 3<sup>rd</sup>. Affected residents will be receiving door to door notices. **Please do not park vehicles on these streets Saturday so work can proceed unimpeded.****

**Final Site Cleanup:** As final paving and restoration is completed the contractor will be doing general site cleanup and taking care of miscellaneous construction items needed to complete the project. Hauling away debris, removing traffic control, hauling out equipment & materials, etc. will be ongoing throughout the week.

**Pavement Marking:** Centerlines, fog lines, turn lanes, crosswalks and stop bars will be painted after the final layer of asphalt is completed.

**Saw and Seal:** Sawing and sealing of joints in the new asphalt surface will occur on 22<sup>nd</sup> St, Cannon St, and 15<sup>th</sup> St W. Crews will be sawing joints to every manhole, gate valve and catch basin structure, and roughly every 40 feet along the streets. The newly sawed joints are then cleaned out and filled with a bituminous sealant.

**THANK YOU! For your cooperation, patience, and understanding during the project**



*An example of final paving operations in progress.*



*A tack truck applying tack coat in advance of the final layer of pavement. Tack coat ensures that the final layer of asphalt will bond to the lower layers to stay in place.*


**Who do I contact with questions or for assistance?** Project management services are being provided by the City's Engineering Department. The department can be reached at **(651) 480-2334** with project questions and concerns.

**Spread the Word & Encourage E-Updates!** Please make sure to share this information with your neighbors and tenants, and encourage them to sign up for at least one of the two electronic updates options if they have not yet done so!

- **E-Notifications** - Sign up for email updates on our website at [www.hastingsmn.gov](http://www.hastingsmn.gov). Click on the *E-notifications* button at the bottom of the page, and sign up for "2020 Neighborhood Infrastructure Improvements".
- **Text Messages** – this is a great way to have the information in the palm of your hand! You'll receive a weekly text message from us with a direct web link to the current construction update. Text **2020STREETS** to **888777** to enroll. Reply STOP at any point to opt out.



15<sup>th</sup> St Area

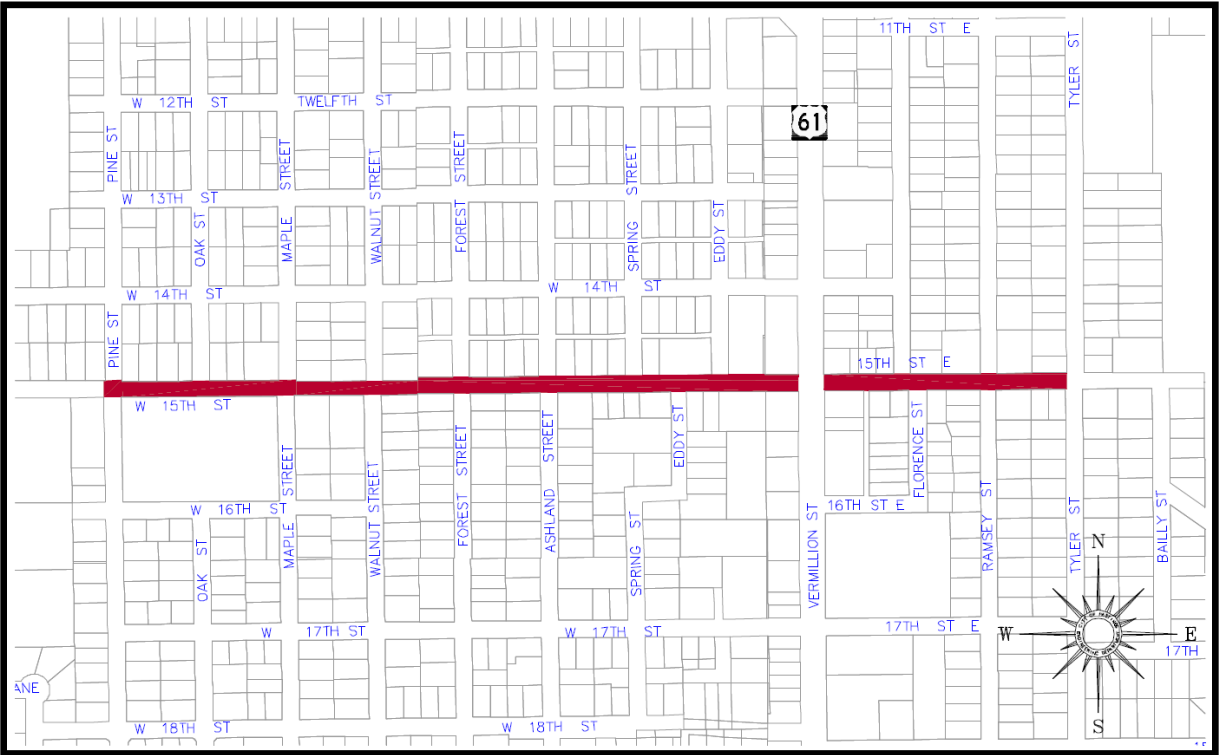

Cannon St Area

